Activity ID	Activity Name	RMNG DUR	Start	Finish
DMNS - Education and Collection Facility		515	31-Jan-11 A	29-Aug-13
PRECONSTRUCTION		494	01-Jul-11 A	31-Jul-13
BIDDING (PHASE 2)		16	01-Jul-11 A	13-Sep-11
Permit Approval		16	01-Jul-11 A	13-Sep-11
A3090	Plan Correction Notice	5	01-Jul-11 A	26-Aug-11
A3100	Plan Correction Response	10	29-Aug-11	12-Sep-11
A3110	Issue Permit	1	13-Sep-11	13-Sep-11
CONSTRUCTION PHASE SUSTAINABILITY		494	12-Aug-11 A	31-Jul-13
A3160	Sustainabilty Submittal Reviews	244	12-Aug-11 A	06-Aug-12
A3170	Prepare LEED Submittal	125	07-Aug-12	04-Feb-13
A3180	Finalize LEED Submittal	125	05-Feb-13	31-Jul-13
PERMIT		25	30-Jun-11 A	26-Sep-11
A4130	Construction Permit	19	30-Jun-11 A	16-Sep-11
A4140	Parks Permit	1	15-Aug-11 A	22-Aug-11
A4120	Demo Permit	14	22-Aug-11	09-Sep-11
A4100	Shoring Permit	15	23-Aug-11*	13-Sep-11
A4150	Waste Water Permit	10	13-Sep-11	26-Sep-11
A4160	Denver Water Permit	10	13-Sep-11	26-Sep-11
PREPATORY WORK		19	31-Jan-11 A	16-Sep-11
A1240	North Dock Bidding/Permitting/Construction	18	31-Jan-11 A	15-Sep-11
A1080	Mobilize Staging	14	22-Aug-11*	09-Sep-11
A2360	Temp Exterior Partitions @ 3rd Floor (Dust)	5	22-Aug-11	26-Aug-11
A3240	Submit Demo Permit	0	22-Aug-11*	
A2390	Exterior Protection	4	08-Sep-11*	13-Sep-11
A2370	Curtain Wall Demo	5	09-Sep-11	15-Sep-11
A2380	Precast Demo	5	09-Sep-11	15-Sep-11
A3250	Issue Demo Permit	0	09-Sep-11*	
A3260	Ground Breaking Ceremony	0	13-Sep-11*	
A1070	Demo Site Hardscape	3	14-Sep-11*	16-Sep-11
A2430	Sue Open	0	14-Sep-11	
CONSTRUCTION		515	22-Aug-11	29-Aug-13
RELOCATE FOR UTILITIES MUSEUM		35	22-Aug-11	10-Oct-11
A1140	Install Fence at Trees	2	22-Aug-11	23-Aug-11
A2460	Install Construction Fence	2	23-Aug-11	24-Aug-11

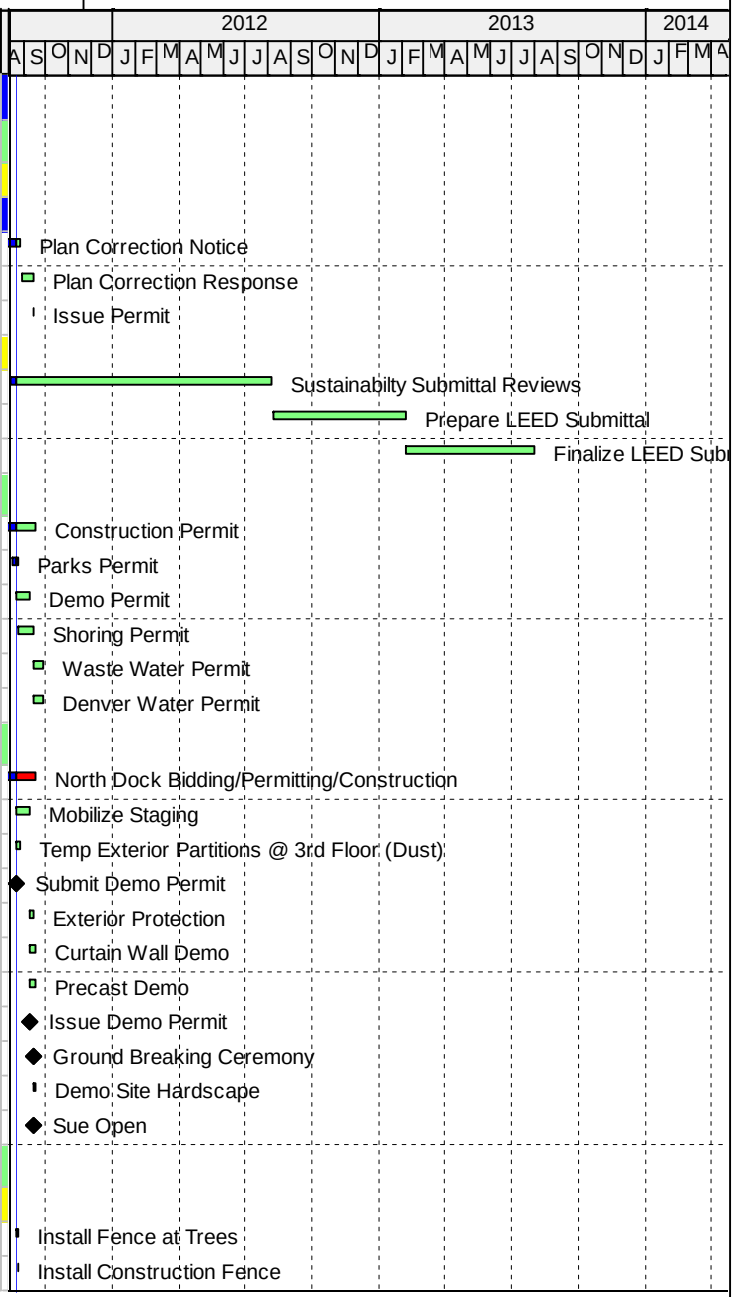

Actual Work
Remaining Work
Critical Remaining Work
Milestone

GH Phipps Construction Companies

Activity ID	Activity Name	RMNG DUR	Start	Finish
A2660	Demo Xcel Street Light & Power	4	06-Sep-11*	09-Sep-11
A2650	Mulch & Prep Tree for Construction	4	09-Sep-11*	14-Sep-11
A3700	Demo/Abanden Elec./Phone/Data (Owners)	3	14-Sep-11	16-Sep-11
A3840	Pothole Exisitng Utilities	5	14-Sep-11	20-Sep-11
A3850	Demo Waterline	5	21-Sep-11	27-Sep-11
A3860	Demo/Install Temp Sanitary Line	5	28-Sep-11	04-Oct-11
A3870	Demo/Install Storm Line	9	28-Sep-11	10-Oct-11
SITEWORK		168	01-Sep-11	30-Apr-12
EXCAVATION		168	01-Sep-11	30-Apr-12
A2290	Install/Open Temp Road	6	01-Sep-11*	09-Sep-11
A3880	Shoring Handrail	5	22-Sep-11*	28-Sep-11
A2410	Complete Dock Demo	5	06-Oct-11	12-Oct-11
A1160	Excavation	65	07-Oct-11	11-Jan-12
A1180	Shoring Sytems	60	07-Oct-11	04-Jan-12
A1170	Over-Excav. & Compaction	10	12-Jan-12	25-Jan-12
A2300	Close/Remove Temp Road	6	23-Apr-12*	30-Apr-12
FOUNDATION/STRUCTURAL		244	12-Jan-12	26-Dec-12
A1000	Caisson (1-Rig) Grids A-L	10	12-Jan-12	25-Jan-12
A3280	Caisson (1-Rig) Grids L-U	10	26-Jan-12	08-Feb-12
Elevator/Stair Cores		36	26-Jan-12	15-Mar-12
A1010	Core Pour 1	6	26-Jan-12	02-Feb-12
A3290	Core Pour 2	6	03-Feb-12	10-Feb-12
A3300	Core Pour 3	6	13-Feb-12	20-Feb-12
A3310	Core Pour 4	6	21-Feb-12	28-Feb-12
A3320	Core Pour 5	6	29-Feb-12	07-Mar-12
A3330	Core Pour 6	6	08-Mar-12	15-Mar-12
1st Lift - B-2 to B-1 Foundation Wall		40	03-Feb-12	29-Mar-12
One Sided		23	03-Feb-12	06-Mar-12
A3340	Pour 1	13	03-Feb-12	21-Feb-12
A3350	Pour 2	10	22-Feb-12	06-Mar-12
Two Sided		31	16-Feb-12	29-Mar-12
A3360	Pour 1	5	16-Feb-12	22-Feb-12
A3370	Pour 2	6	23-Feb-12	01-Mar-12
A3380	Pour 3	5	02-Mar-12	08-Mar-12
A3390	Pour 4	5	09-Mar-12	15-Mar-12
A3400	Pour 5	5	16-Mar-12	22-Mar-12
A3410	Pour 6	5	23-Mar-12	29-Mar-12

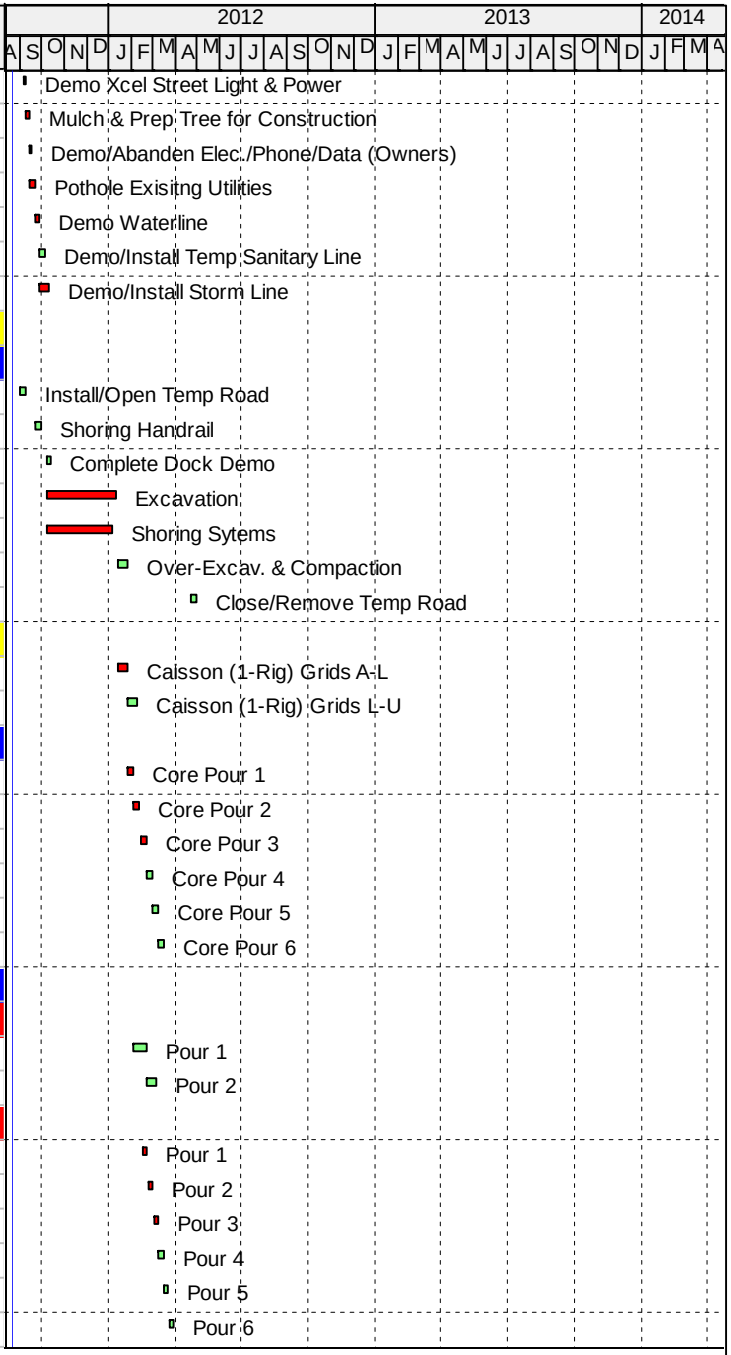

Actual Work
Remaining Work
Critical Remaining Work
Milestone

DMNS - Education and Collection Facility

GHPhipps CONSTRUCTION COMPANIES

Activity ID	Activity Name	RMNG DUR	Start	Finish
S.O.G.		42	02-Mar-12	30-Apr-12
Grids L-U		23	02-Mar-12	03-Apr-12
A3420	Rough-in MEP/Drainage	13	02-Mar-12	20-Mar-12
A3430	Slab Waterproof System	4	21-Mar-12	26-Mar-12
A3440	Sand	5	27-Mar-12	02-Apr-12
A3450	Pour	1	03-Apr-12	03-Apr-12
Grids A-L		22	30-Mar-12	30-Apr-12
A3460	Rough-in MEP/Drainage	13	30-Mar-12	17-Apr-12
A3470	Slab Waterproof System	3	18-Apr-12	20-Apr-12
A3480	Sand	5	23-Apr-12	27-Apr-12
A3490	Pour	1	30-Apr-12	30-Apr-12
Deck B-1		32	04-Apr-12	17-May-12
Grids O.4 to P		14	04-Apr-12	23-Apr-12
A3500	Deck	9	04-Apr-12	16-Apr-12
A3510	Rebar/MEP	6	13-Apr-12	20-Apr-12
A3520	Pour	1	23-Apr-12	23-Apr-12
Grids F.5 to O,4		14	17-Apr-12	04-May-12
A3530	Deck	9	17-Apr-12	27-Apr-12
A3540	Rebar/MEP	6	26-Apr-12	03-May-12
A3550	Pour	1	04-May-12	04-May-12
Grids A to F.5		14	30-Apr-12	17-May-12
A3560	Deck	9	30-Apr-12	10-May-12
A3570	Rebar/MEP	6	09-May-12	16-May-12
A3580	Pour	1	17-May-12	17-May-12
Walls 2nd Lift B-1 to 100 Foundation Walls		36	24-Apr-12	13-Jun-12
A3620	Pour 1	7	24-Apr-12	02-May-12
A3630	Pour 2	6	03-May-12	10-May-12
A3680	1-Sided Pour - Pour #1	14	07-May-12	24-May-12
A3640	Pour 3	6	11-May-12	18-May-12
A3650	Pour 4	6	21-May-12	29-May-12
A3690	1-Sided Pour - Pour #2	11	25-May-12	11-Jun-12
A3660	Pour 5	6	30-May-12	06-Jun-12
A3670	Pour 6	5	07-Jun-12	13-Jun-12
Deck Level 1		67	21-May-12	23-Aug-12
Grids O.4 to U		22	21-May-12	20-Jun-12
A3710	Deck	13	21-May-12	07-Jun-12
A3720	Rebar/MEP	10	06-Jun-12	19-Jun-12

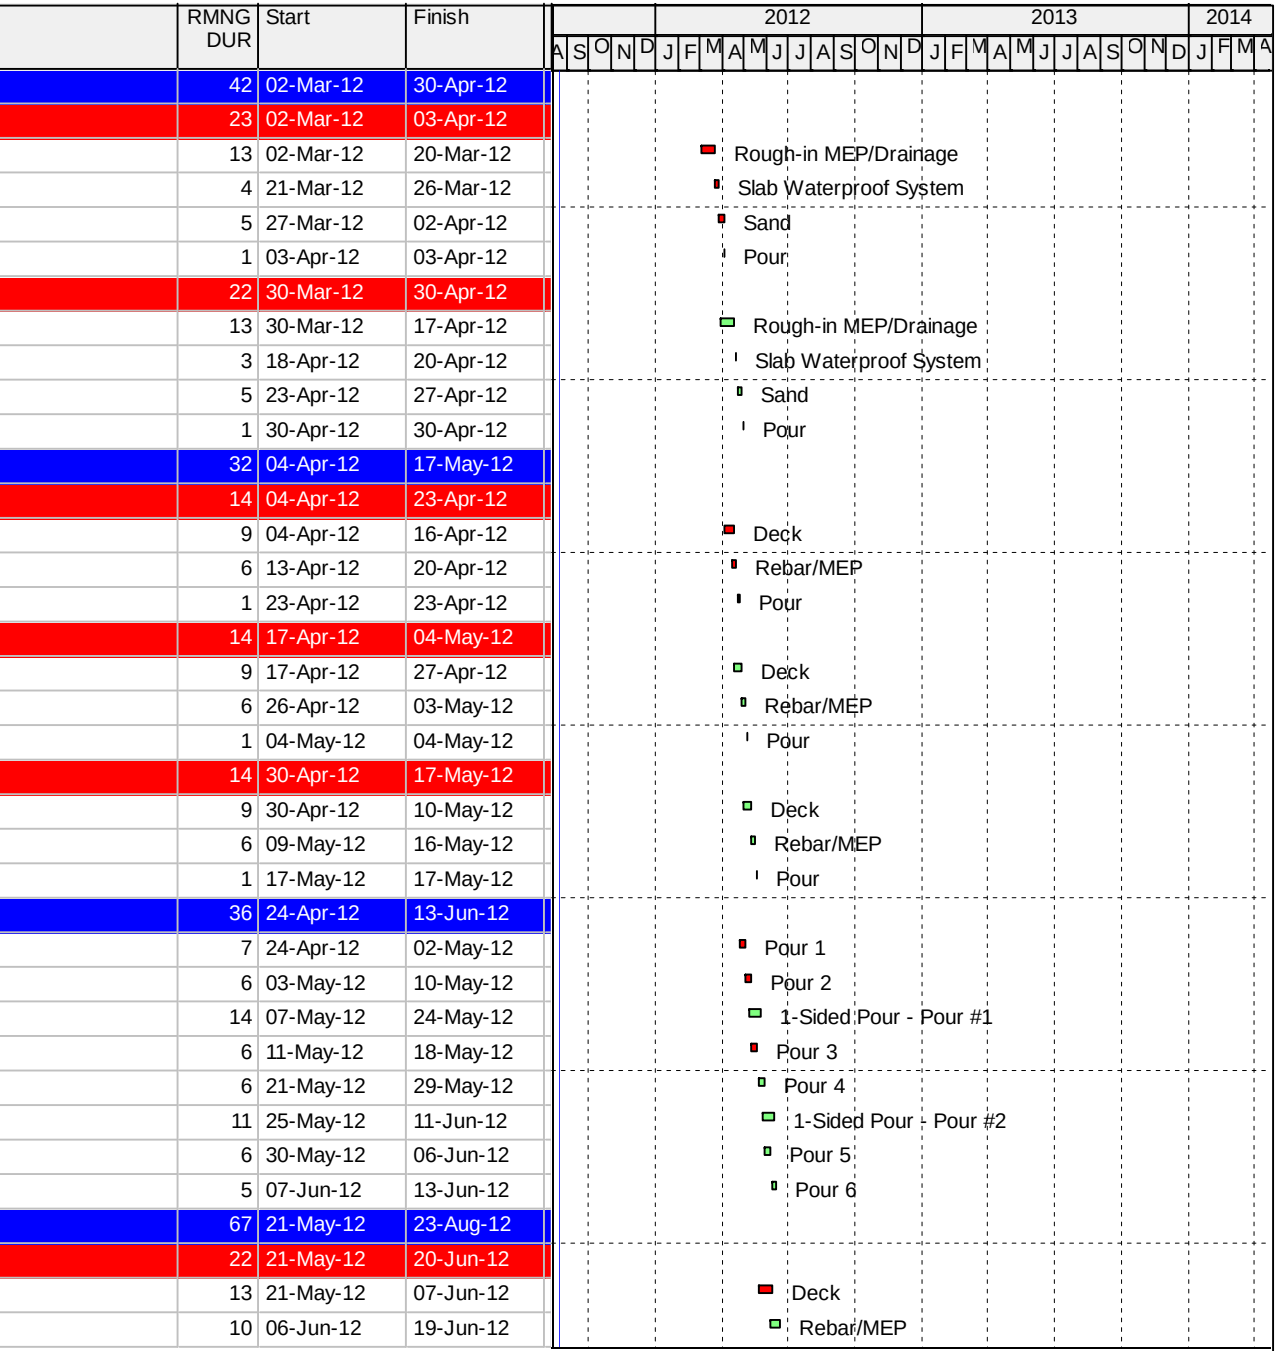

Actual Work
Remaining Work
Critical Remaining Work
Milestone

DMNS - Education and Collection Facility

GH Phipps CONSTRUCTION COMPANIES

Activity ID	Activity Name	RMNG DUR	Start	Finish
A3730	Pour	1	20-Jun-12	20-Jun-12
Grids F.5 to O.4		18	08-Jun-12	03-Jul-12
A3740	Deck	10	08-Jun-12	21-Jun-12
A3750	Rebar/MEP	9	20-Jun-12	02-Jul-12
A3760	Pour	1	03-Jul-12	03-Jul-12
Grids A to F.5		44	22-Jun-12	23-Aug-12
A3770	Deck	13	22-Jun-12	11-Jul-12
A3780	Rebar/MEP	10	10-Jul-12	23-Jul-12
A3790	Pour	1	24-Jul-12	24-Jul-12
A3800	Strip & Cure	22	25-Jul-12	23-Aug-12
2nd Floor		77	25-Jul-12	09-Nov-12
A2420	Interior Demo & Micropiles/Caissons	30	25-Jul-12	05-Sep-12
A1190	Structural Steel	6	30-Jul-12	06-Aug-12
A3810	Detail & Deck	8	06-Aug-12	15-Aug-12
A1200	Topping on Metal Deck	6	04-Sep-12	11-Sep-12
A1250	Fireproofing	15	22-Oct-12	09-Nov-12
3rd Floor		81	09-Aug-12	04-Dec-12
A1210	Structural Steel	6	09-Aug-12	16-Aug-12
A3820	Detail & Deck	8	17-Aug-12	28-Aug-12
A1220	Topping on Metal Deck	6	12-Sep-12	19-Sep-12
A1260	Fireproofing	15	12-Nov-12	04-Dec-12
Penthouse/Roof		82	22-Aug-12	18-Dec-12
A1230	Structural Steel	4	22-Aug-12	27-Aug-12
A3830	Detail & Deck	5	27-Aug-12	31-Aug-12
A2440	Topping on Metal Deck	5	04-Sep-12	10-Sep-12
A1270	Fireproofing	10	05-Dec-12	18-Dec-12
Penthouse Roof		83	28-Aug-12	26-Dec-12
A2450	Structural Steel/Deck	4	28-Aug-12	31-Aug-12
A3270	Structural Top Out	0		31-Aug-12
A2470	Fireproofing	5	19-Dec-12	26-Dec-12
ENCLOSURE		185	13-Jul-12	04-Apr-13
A2220	Exterior Skin Mock-up	0	13-Jul-12	
A1300	Exterior Stud Framing	13	25-Sep-12	11-Oct-12
A1310	Gyp Sheathing	12	03-Oct-12	18-Oct-12
A1290	Roof System	11	05-Oct-12	19-Oct-12
A1320	Rigid Insulation & Membrane	15	05-Oct-12	25-Oct-12
A1280	Metal Panels	15	12-Oct-12	01-Nov-12

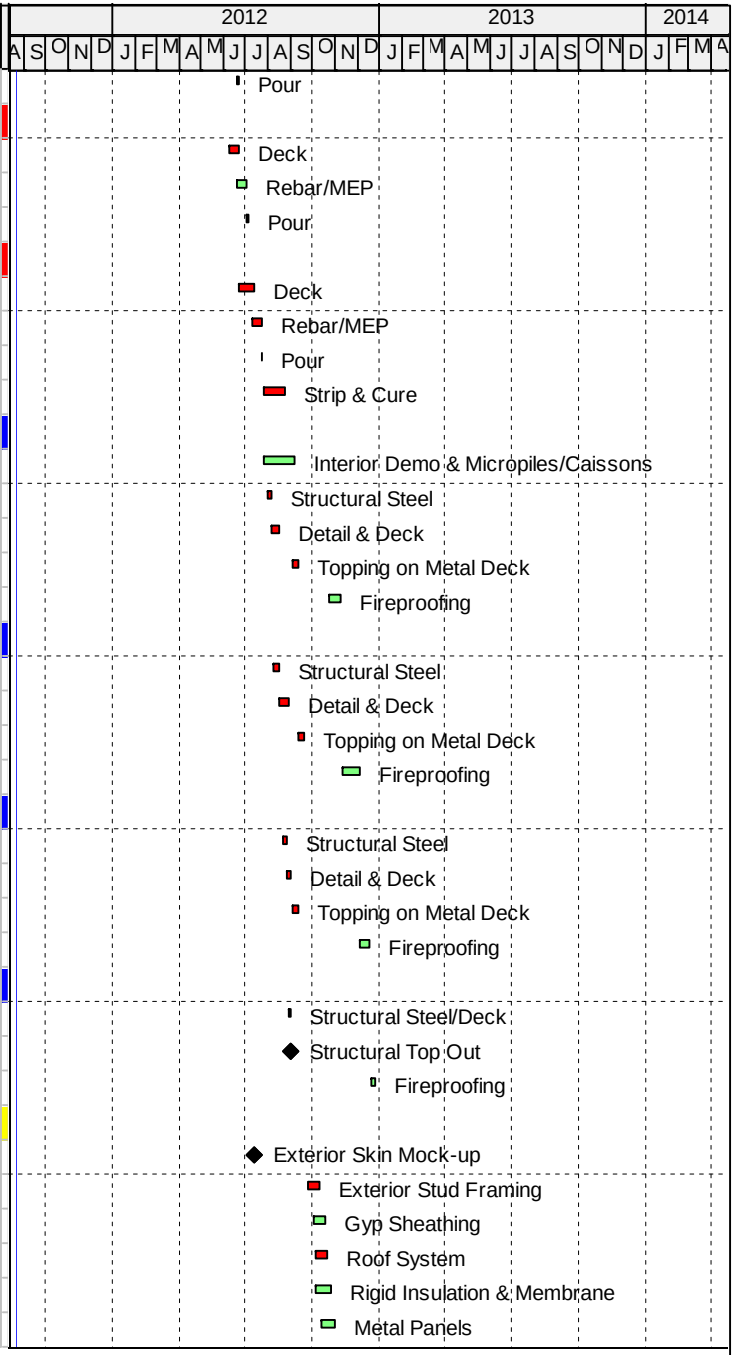

Actual Work
Remaining Work
Critical Remaining Work
Milestone

DMNS - Education and Collection Facility

GH Phipps CONSTRUCTION COMPANIES

Activity ID	Activity Name	RMNG DUR	Start	Finish
A1340	Stone Wall System	36	12-Oct-12	04-Dec-12
A4010	Curtain Wall	48	09-Nov-12	21-Jan-13
A2240	Punched Windows	15	15-Jan-13	04-Feb-13
A2310	Solar Shades	20	15-Jan-13	11-Feb-13
A1330	Waterproofing - Plaza Area	19	12-Feb-13	08-Mar-13
A2230	Pavers and Hardscape Plaza	19	11-Mar-13	04-Apr-13
ROUGH-INS		135	24-Aug-12	07-Mar-13
B-2		113	24-Aug-12	05-Feb-13
RO--.1650	Waste and Vent Rough	5	24-Aug-12	30-Aug-12
RO--.1660	Install Major Mechanical Equipment	15	24-Aug-12	14-Sep-12
RO--.1690	R/I - Mechanical Shafts	30	24-Aug-12	05-Oct-12
RO--.1670	Hang Ductwork/Major Mech Equipment	25	31-Aug-12	05-Oct-12
RO--.1680	R/I - Mechanical Room	40	31-Aug-12	26-Oct-12
RO--.1720	Overhead HVAC Piping Rough	20	08-Oct-12	02-Nov-12
RO--.1750	Overhead Elec Rough	20	08-Oct-12	02-Nov-12
RO--.1700	Purge Cavity Framing	16	08-Oct-12	29-Oct-12
RO--.1710	Interior Walls Framing	16	17-Oct-12	07-Nov-12
RO--.1740	Fire Prot Rough	15	05-Nov-12	27-Nov-12
RO--.1830	MEP Rough (walls)	20	08-Nov-12	07-Dec-12
RO--.1640	Roof Drain Leader Rough	8	20-Nov-12	03-Dec-12
RO--.1873	Purge Cavity Hang Sheet Rock Walls	20	10-Dec-12	08-Jan-13
RO--.2383	Interior Walls Hang Sheet Rock Walls	20	09-Jan-13	05-Feb-13
B-1		135	24-Aug-12	07-Mar-13
RO--.1893	Waste and Vent Rough	15	24-Aug-12	14-Sep-12
RO--.1903	Hang Ductwork/Major Mech Equipment	25	17-Sep-12	19-Oct-12
RO--.1913	Overhead HVAC Piping Rough	20	22-Oct-12	16-Nov-12
RO--.1933	Overhead Elec Rough	20	22-Oct-12	16-Nov-12
RO--.2393	Purge Cavity Framing Walls	15	22-Oct-12	09-Nov-12
RO--.2403	Interior Walls Framing	15	31-Oct-12	20-Nov-12
RO--.1883	Roof Drain Leader Rough	12	02-Nov-12	19-Nov-12
RO--.2433	Purge Cavity Framing Ceilings	20	12-Nov-12	11-Dec-12
RO--.1923	Fire Prot Rough	15	19-Nov-12	11-Dec-12
RO--.1963	MEP Rough (walls)	20	12-Dec-12	10-Jan-13
RO--.2413	Purge Cavity Hang Sheet Rock Walls	15	11-Jan-13	31-Jan-13
RO--.2423	Interior Walls Hang Sheet Rock Walls	15	01-Feb-13	21-Feb-13
RO--.2443	Purge Cavity Hang Sheet Rock Ceilings	15	15-Feb-13	07-Mar-13
1st Floor		73	29-Oct-12	12-Feb-13

Actual Work
Remaining Work
Critical Remaining Work
Milestone

DMNS - Education and Collection Facility

GH Phipps CONSTRUCTION COMPANIES

Activity ID	Activity Name	RMNG DUR	Start	Finish
RO--.1983	Roof Drain Leader Rough	4	29-Oct-12	01-Nov-12
RO--.1993	Waste and Vent Rough	10	29-Oct-12	09-Nov-12
RO--.2003	Hang Ductwork	20	12-Nov-12	11-Dec-12
RO--.2013	Overhead HVAC Piping Rough	15	12-Dec-12	03-Jan-13
RO--.2033	Overhead Elec Rough	20	12-Dec-12	10-Jan-13
RO--.2053	Int Met Studs	13	12-Dec-12	31-Dec-12
RO--.2063	MEP Rough (walls)	15	02-Jan-13	22-Jan-13
RO--.2023	Fire Prot Rough	10	11-Jan-13	24-Jan-13
RO--.2073	Hang Sheet Rock Walls	15	23-Jan-13	12-Feb-13
2nd Floor		79	23-Oct-12	14-Feb-13
RO--.2083	Roof Drain Leader Rough	4	23-Oct-12	26-Oct-12
RO--.2093	Waste and Vent Rough	5	12-Nov-12	16-Nov-12
RO--.2103	Hang Ductwork	20	19-Nov-12	18-Dec-12
RO--.2113	Overhead HVAC Piping Rough	15	19-Dec-12	10-Jan-13
RO--.2133	Overhead Elec Rough	15	19-Dec-12	10-Jan-13
RO--.2153	Int Met Studs	10	19-Dec-12	03-Jan-13
RO--.2163	MEP Rough (walls)	15	04-Jan-13	24-Jan-13
RO--.2123	Fire Prot Rough	10	11-Jan-13	24-Jan-13
RO--.2173	Hang Sheet Rock Walls	15	25-Jan-13	14-Feb-13
3rd Floor		96	05-Oct-12	21-Feb-13
RO--.2183	Roof Drain Leader Rough	12	05-Oct-12	22-Oct-12
RO--.2193	Waste and Vent Rough	5	19-Nov-12	27-Nov-12
RO--.2203	Hang Ductwork	20	28-Nov-12	26-Dec-12
RO--.2213	Overhead HVAC Piping Rough	15	27-Dec-12	17-Jan-13
RO--.2233	Overhead Elec Rough	15	27-Dec-12	17-Jan-13
RO--.2253	Int Met Studs	10	27-Dec-12	10-Jan-13
RO--.2263	MEP Rough (walls)	15	11-Jan-13	31-Jan-13
RO--.2223	Fire Prot Rough	10	18-Jan-13	31-Jan-13
RO--.2273	Hang Sheet Rock Walls	15	01-Feb-13	21-Feb-13
PENTHOUSE		75	22-Oct-12	07-Feb-13
RO--.2343	Major Mechanical	5	22-Oct-12	26-Oct-12
RO--.2283	Roof Drain Leader Rough	8	23-Oct-12	01-Nov-12
RO--.2293	Waste and Vent Rough	5	28-Nov-12	04-Dec-12
RO--.2303	Hang Ductwork/Major Mech Equipment	20	05-Dec-12	03-Jan-13
RO--.2313	Overhead HVAC Piping Rough	15	04-Jan-13	24-Jan-13
RO--.2333	Overhead Elec Rough	15	04-Jan-13	24-Jan-13
RO--.2353	Int Met Studs	5	04-Jan-13	10-Jan-13

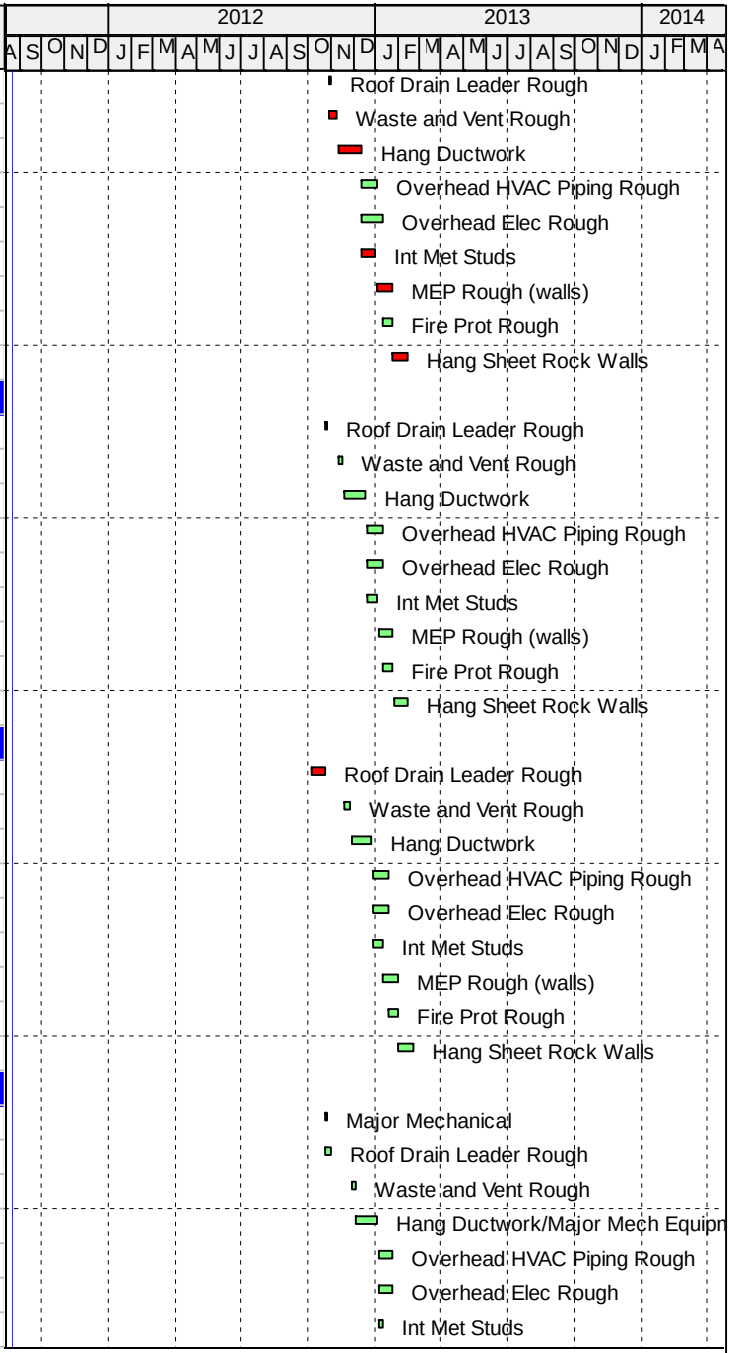

Actual Work
Remaining Work
Critical Remaining Work
Milestone

DMNS - Education and Collection Facility

GHPhipps CONSTRUCTION COMPANIES

Activity ID	Activity Name	RMNG DUR	Start	Finish
RO--.2363	MEP Rough (walls)	5	11-Jan-13	17-Jan-13
RO--.2373	Hang Sheet Rock Walls	9	18-Jan-13	30-Jan-13
RO--.2323	Fire Prot Rough	10	25-Jan-13	07-Feb-13
INTERIOR FINISHES		157	20-Dec-12	01-Aug-13
B-2		99	23-Jan-13	11-Jun-13
A1350	Purge Cavity Tape & Finish	12	23-Jan-13	07-Feb-13
A3940	Interior Walls Tape & Finish	12	08-Feb-13	25-Feb-13
A1450	Rails	15	26-Feb-13	18-Mar-13
A1360	Prime & Paint	10	19-Mar-13	01-Apr-13
A1370	1st Coat Paint	5	02-Apr-13	08-Apr-13
A1390	Acoustical Ceiling	5	02-Apr-13	08-Apr-13
A1380	Hang Doors	10	09-Apr-13	22-Apr-13
A1430	Fume Hoods	5	09-Apr-13	15-Apr-13
A1440	Unistrut	5	09-Apr-13	15-Apr-13
A1410	Flooring	20	23-Apr-13	20-May-13
A1420	Lab Tables/Casework	5	07-May-13	13-May-13
A2080	FFE	25	07-May-13	11-Jun-13
A2280	Final Paint	5	13-May-13	17-May-13
A1710	GHP Cleanup & Punchlist	5	14-May-13	20-May-13
B-1		103	08-Mar-13	01-Aug-13
A1460	Purge Cavity Tape & Finish	15	08-Mar-13	28-Mar-13
A3950	Interior Walls Tape & Finish	15	29-Mar-13	18-Apr-13
A1750	Rails	15	19-Apr-13	09-May-13
A1510	Prime & Paint	8	10-May-13	21-May-13
A1560	1st Coat Paint	5	22-May-13	29-May-13
A1610	Hang Doors	10	22-May-13	05-Jun-13
A1660	Acoustical Ceiling	5	22-May-13	29-May-13
A1700	Flooring	20	30-May-13	26-Jun-13
A3970	Final Paint	5	04-Jun-13	10-Jun-13
A1720	Lab Tables/Casework	30	13-Jun-13	25-Jul-13
A1730	Fume Hoods	5	18-Jun-13	24-Jun-13
A1740	Unistrut	5	27-Jun-13	03-Jul-13
A1760	GHP Cleanup & Punchlist	5	26-Jul-13	01-Aug-13
1st Floor		102	20-Dec-12	14-May-13
A4090	New Bathroom Existing	16	20-Dec-12*	14-Jan-13
A1470	Tape & Finish	10	13-Feb-13	26-Feb-13
A1520	Prime & Paint	10	27-Feb-13	12-Mar-13

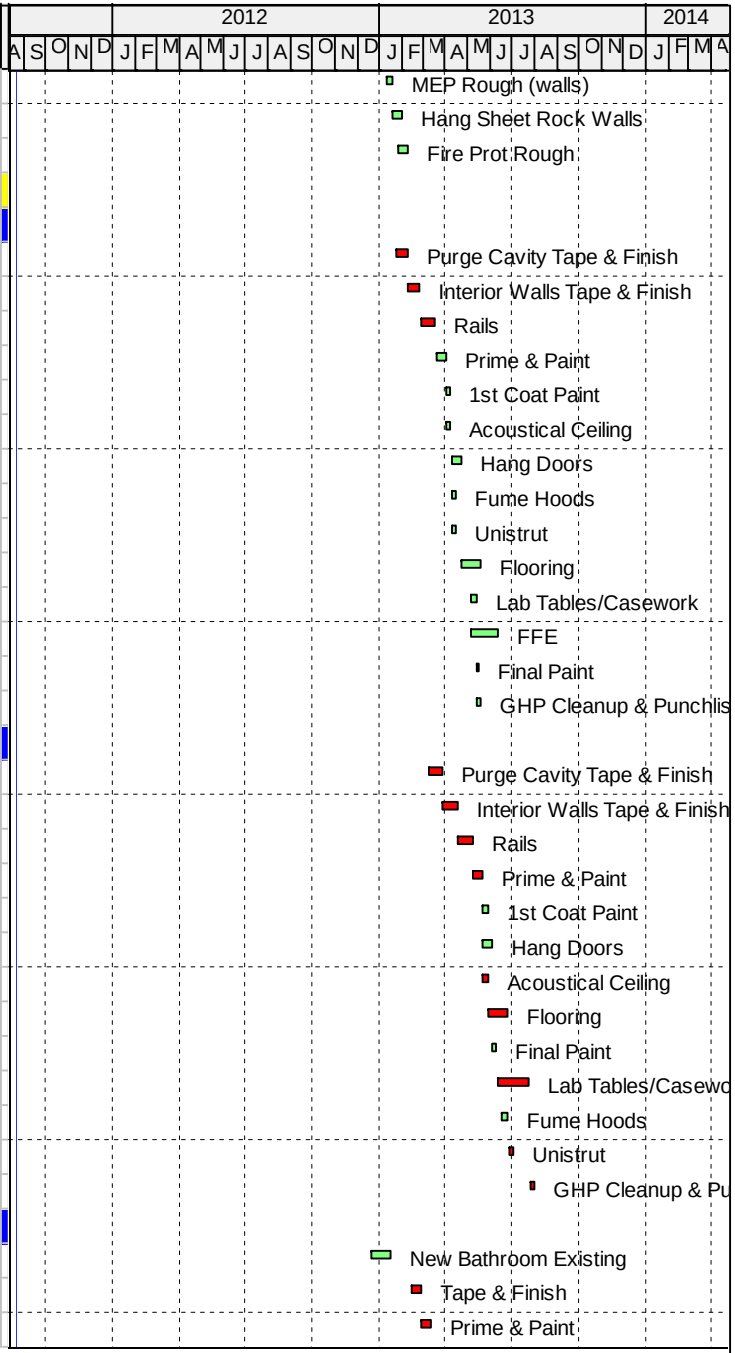

Actual Work
Remaining Work
Critical Remaining Work
Milestone

DMNS - Education and Collection Facility

GHPhipps CONSTRUCTION COMPANIES

Activity ID	Activity Name	RMNG DUR	Start	Finish
A1570	1st Coat Paint	10	13-Mar-13	26-Mar-13
A1620	Hang Doors/Casework	10	13-Mar-13	26-Mar-13
A1670	Acoustical Ceiling	5	13-Mar-13	19-Mar-13
A1770	Acoustical Panels	10	20-Mar-13	02-Apr-13
A1790	Terazzo	35	20-Mar-13	07-May-13
A1810	Carpet	35	20-Mar-13	07-May-13
A2320	Stone	35	20-Mar-13	07-May-13
A2350	Epoxy Flooring @ Dirty Prep	5	20-Mar-13	26-Mar-13
A1820	Glass Wall Forum	15	27-Mar-13	16-Apr-13
A4020	Glass Wall Studio	15	27-Mar-13	16-Apr-13
A1800	Operable Wall Studio	10	03-Apr-13	16-Apr-13
A3980	Final Paint	5	03-Apr-13	09-Apr-13
A1830	GHP Cleanup & Punchlist	5	08-May-13	14-May-13
2nd Floor		87	20-Dec-12	23-Apr-13
A4080	New Bathroom Existing	16	20-Dec-12*	14-Jan-13
A1480	Tape & Finish	10	15-Feb-13	28-Feb-13
A1530	Prime & Paint	10	01-Mar-13	14-Mar-13
A1580	1st Coat Paint	10	15-Mar-13	28-Mar-13
A1630	Hang Doors	5	15-Mar-13	21-Mar-13
A1680	Acoustical Ceiling	5	15-Mar-13	21-Mar-13
A1840	Acoustical Panels	10	22-Mar-13	04-Apr-13
A1850	Metal Ceiling	10	22-Mar-13	04-Apr-13
A1870	Sport Floor (OWNER)	3	22-Mar-13	26-Mar-13
A1890	Unistrut	10	27-Mar-13	09-Apr-13
A1900	Glass Wall	15	27-Mar-13	16-Apr-13
A4060	Glass Store Front	15	27-Mar-13	16-Apr-13
A4070	Glass Handrail	15	27-Mar-13	16-Apr-13
A4030	Terazzo	15	29-Mar-13	18-Apr-13
A4040	Carpet	15	29-Mar-13	18-Apr-13
A4050	VCT	15	29-Mar-13	18-Apr-13
A3990	Final Paint	5	08-Apr-13	12-Apr-13
A1910	GHP Cleanup & Punchlist	5	17-Apr-13	23-Apr-13
3rd Floor		94	20-Dec-12	02-May-13
A1780	New Bathroom Existing	16	20-Dec-12*	14-Jan-13
A1490	Tape & Finish	10	22-Feb-13	07-Mar-13
A1540	Prime & Paint	10	08-Mar-13	21-Mar-13
A1590	1st Coat Paint	10	22-Mar-13	04-Apr-13

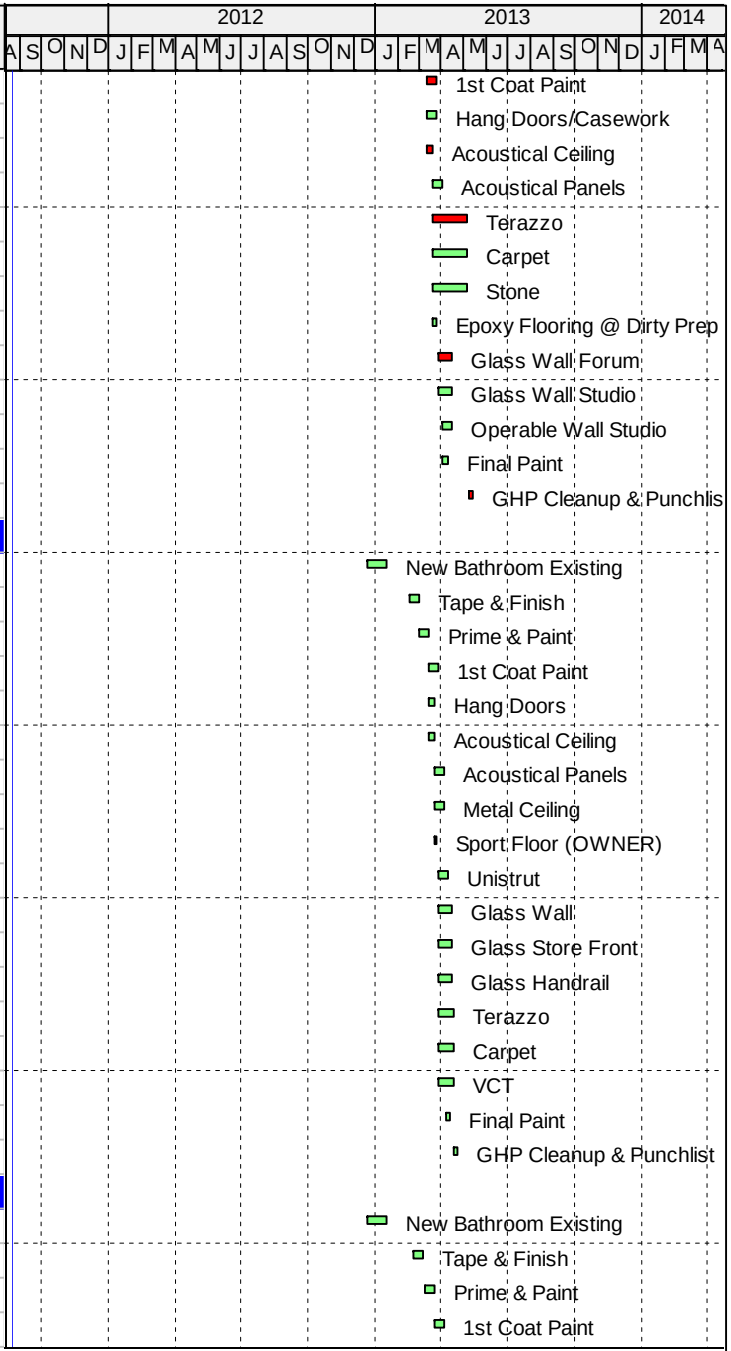

Actual Work ◆ Milestone

Remaining Work

Critical Remaining Work

DMNS - Education and Collection Facility

GHPhipps CONSTRUCTION COMPANIES

Activity ID	Activity Name	RMNG DUR	Start	Finish
A1640	Hang Doors	5	22-Mar-13	28-Mar-13
A1690	Acoustical Ceiling	5	22-Mar-13	28-Mar-13
A1930	Metal @ Mezzanines	10	25-Mar-13	05-Apr-13
A1920	Lineal Metal Ceiling	15	29-Mar-13	18-Apr-13
A2090	Patch Terrazzo	5	29-Mar-13	04-Apr-13
A1940	Unistrut/Vapor Barrier	10	10-Apr-13	23-Apr-13
A1860	Acoustical Panels	11	10-Apr-13	24-Apr-13
A1880	Carpet	5	10-Apr-13	16-Apr-13
A4000	Final Paint	5	19-Apr-13	25-Apr-13
A2330	Glazing @ Bridges and Auto Doors	10	19-Apr-13	02-May-13
A1950	GHP Cleanup & Punchlist	5	24-Apr-13	30-Apr-13
PENTHOUSE		11	31-Jan-13	14-Feb-13
A1500	Tape & Finish	5	31-Jan-13	06-Feb-13
A1550	Prime & Paint	3	07-Feb-13	11-Feb-13
A1600	1st Coat Paint/Final Paint	3	12-Feb-13	14-Feb-13
A1650	Hang Doors	3	12-Feb-13	14-Feb-13
SITEWORK FINISHES		192	24-Aug-12	28-May-13
A2250	Waterproof Foundation Walls	29	24-Aug-12	04-Oct-12
A2260	Backfill Walls	36	31-Aug-12	22-Oct-12
A1960	Waterproof Deck	21	05-Dec-12	04-Jan-13
A1970	Glass Basement Stair	18	07-Jan-13	30-Jan-13
A2510	Plaza Pavers	35	07-Jan-13	22-Feb-13
A1980	Wall Glass	10	31-Jan-13	13-Feb-13
WEST		25	18-Feb-13	22-Mar-13
A1990	Grading/Utilities	10	18-Feb-13	01-Mar-13
A2000	Hardscape	10	04-Mar-13	15-Mar-13
A2010	Landscape	5	18-Mar-13	22-Mar-13
EAST		33	04-Mar-13	17-Apr-13
A2020	Grading/Complete Utilities	5	04-Mar-13	08-Mar-13
A2030	Hardscape	23	18-Mar-13	17-Apr-13
A2040	Landscape	5	25-Mar-13	29-Mar-13
SOUTH		56	11-Mar-13	28-May-13
A2050	Grading/Complete Utilities	10	11-Mar-13	22-Mar-13
A2070	Landscape	20	01-Apr-13	26-Apr-13
A2060	Hardscape	28	18-Apr-13	28-May-13
PROJECT CLOSEOUT		107	01-Apr-13	29-Aug-13
A2110	Submit Preliminary O & M for approval	0	01-Apr-13*	

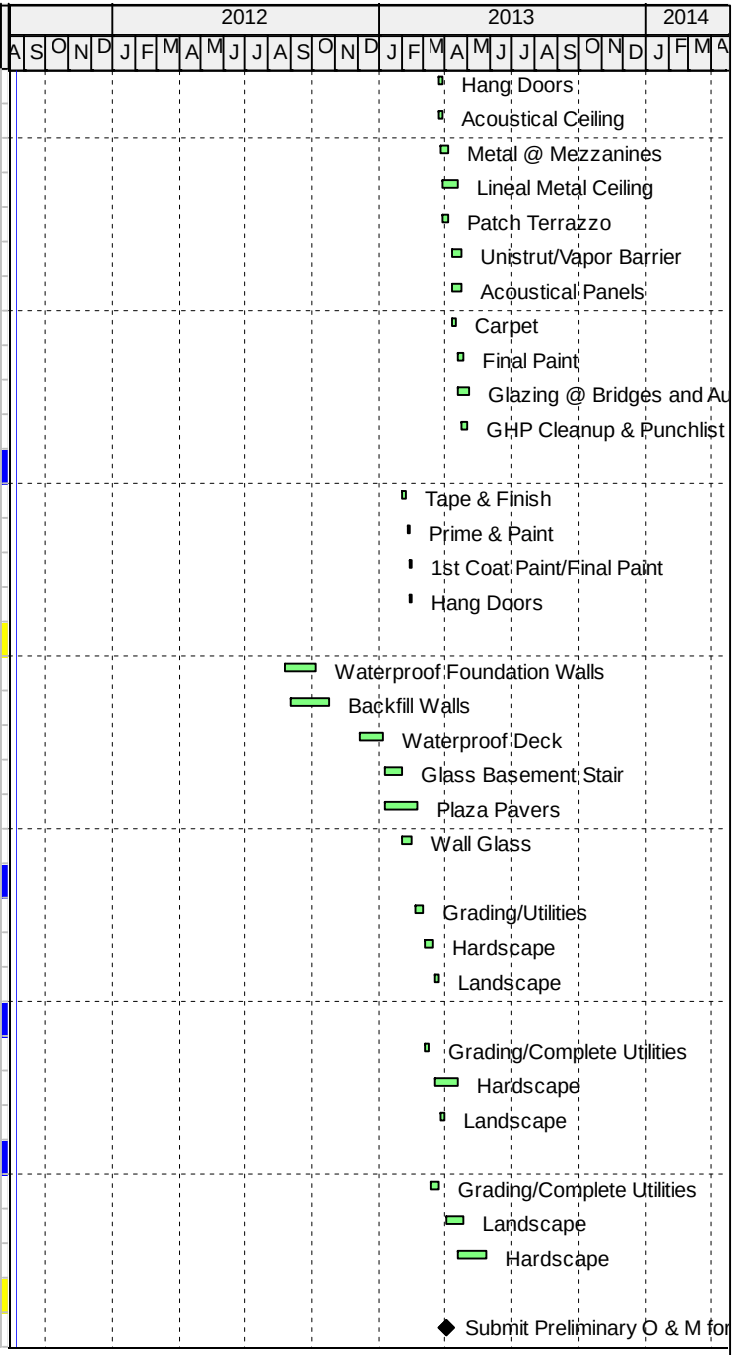

Actual Work
Remaining Work
Critical Remaining Work
Milestone

DMNS - Education and Collection Facility

GHPhipps CONSTRUCTION COMPANIES

Activity ID	Activity Name	RMNG DUR	Start	Finish
A2100	Project Closeout	30	15-May-13	26-Jun-13
A2170	Training	10	15-May-13	29-May-13
A2190	LEED "Burn out period" / commissioning	10	19-Jul-13	01-Aug-13
A2120	Final inspections	5	02-Aug-13	08-Aug-13
A2160	Final punch	5	02-Aug-13	08-Aug-13
A2140	Final fire department testing and inspection	5	09-Aug-13	15-Aug-13
A2130	Final building department inspection	5	16-Aug-13	22-Aug-13
A2180	Final O & M's and Asbuilts	5	23-Aug-13	29-Aug-13
A2200	Certificate of Occupancy	5	23-Aug-13	29-Aug-13
A2210	Substantial Completion	0		29-Aug-13*

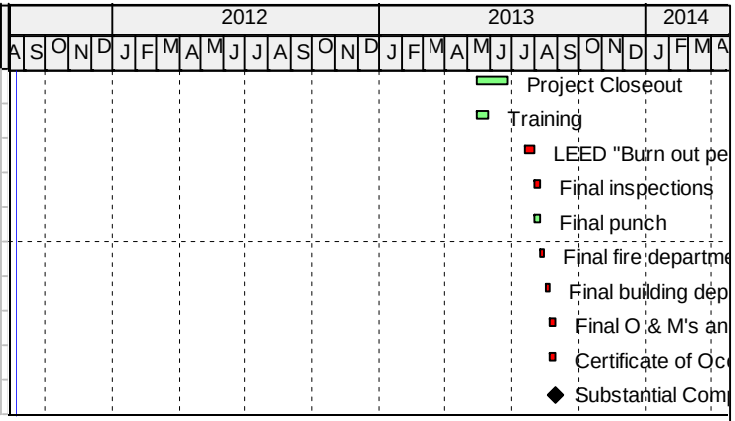

Actual Work
Remaining Work
Critical Remaining Work
Milestone

DMNS - Education and Collection Facility

GHPhipps CONSTRUCTION COMPANIES
